

City of La Quinta

CITY / SA / HA / FA MEETING DATE: June 16, 2015

ITEM TITLE: ACCEPT AVENIDA CARRANZA DRAINAGE IMPROVEMENTS

AGENDA CATEGORY: BUSINESS SESSION: CONSENT CALENDAR: 12 STUDY SESSION: PUBLIC HEARING:

RECOMMENDED ACTION:

Accept the Avenida Carranza Drainage Improvements project as 100 percent complete; authorize the City Clerk to file a Notice of Completion with the Office of the County Recorder; and authorize staff to release retention in the amount of \$1,668, thirty-five days after the Notice of Completion is recorded.

EXECUTIVE SUMMARY:

- This project improved a storm drain located in the area of Avenida Montezuma and Avenida Carranza.
- The work is now complete and staff requests City Council's acceptance of the improvements in order to complete the contract and allow final payment to the contractor.

FISCAL IMPACT:

The following is the final accounting for this project:

Original Contract Amount	\$ 40,792
Contract Change Order No. 1	<u>\$ 1,668</u>
Final Contract Amount	\$ 42,460
Project Budget	\$ 70,000
Final Contract Amount	(\$ 42,460)
Utilities, Plans, and Other Miscellaneous Construction Costs	(\$ 0)

Design, Professional, Testing, Inspection, Survey, Personnel	<u>(\$ 5,086)</u>
Funds Remaining	\$ 22,454

Adequate funding is available to close out this project.

BACKGROUND/ANALYSIS:

This project, which made improvements to a formerly abandoned storm drain to the Oleander Reservoir, is located just north of Avenida Montezuma at the north end of Avenida Carranza (Attachment 1). The improvements included protecting the existing dual pipe inlets with a concrete headwall and trash rack and installing grouted rip rap in front of the pipes in order to slow water coming from the street before entering the pipes.

On March 17, 2015, a contract in the amount of \$40,792 was awarded to Dateland Construction Co., Inc. for these improvements. Subsequently, Contract Change Order No. 1 was issued for the reimbursement of Coachella Valley Water District Permit Fees. There were 15 working days with a completion date of May 8, 2015. No liquidated damages are recommended.


Construction is 100 percent complete and in compliance with the plans and specifications. Staff therefore recommends acceptance of the project and release of the retention thirty-five days after the Notice of Completion is recorded.

ALTERNATIVES:

Since the project has been constructed and reviewed for conformance to the plans and specifications, staff does not recommend any alternatives to the recommended action.

Report prepared by: Ed Wimmer, Principal Engineer Report approved for submission by: Timothy R. Jonasson Public Works Director/City Engineer

Attachment: 1. Vicinity Map

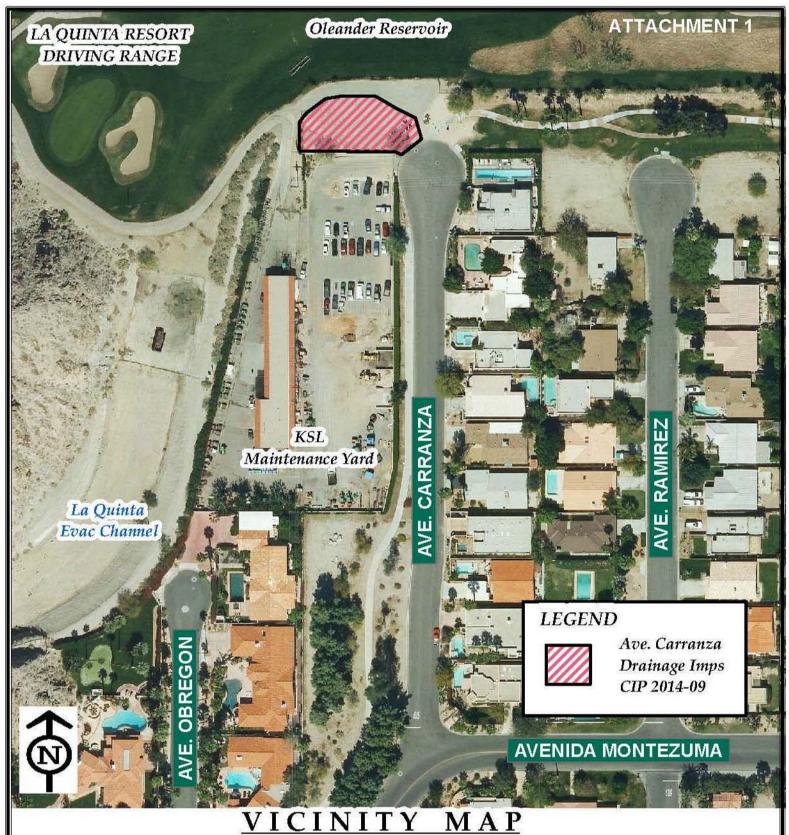

Not to Scale
